Appointment Booking Tool Rollout

Appointment Booking Tool Rollout (Pilot → All Boutiques)

Task	Owner	Status	Due date	Notes	Priority	Dependency	Stakeholder Owner
Plan 3		In progress	Mar 5, 2027	Last update: Pilot scope drafted + success metrics outlined. Next: Finalize workflow + confirm timeline.	Medium		Retail Ops, Boutique ...
Setup 3		In progress	Mar 12, 20...	Last update: Setup checklist created; access plan in progress. Next: Configure appointment types + notification settings.	Medium	Plan	IT/Helpdesk, Managers
Testing 3		Not Started	Mar 19, 20...	Last update: UAT cases drafted. Next: Schedule pilot UAT; track issues to closure.	Medium	Setup	Pilot Users
Training & Comms 4		Not Started	Mar 26, 2...	Last update: Content outline drafted. Next: Build quick guide + mini deck; finalize FAQ.	Medium	Setup, Testing	Training, Store Associ...
Launch + Support 4		Not Started	Apr 2, 2027	Next: Publish go-live checklist + prepare Week 1 adoption update.	High	Training & Comms	All Users, Helpdesk

Rollout tracker coordinating planning, setup, testing, training, and launch activities across pilot boutiques and operational stakeholders.

Task	Owner	Status	Due date	Notes	Priority	Dependency	Stakeholder Owner
Plan 3		In progress	Mar 5, 2027	Last update: Pilot scope drafted + success metrics outlined. Next: Finalize workflow + confirm timeline.	Medium		Retail Ops, Boutique ...

Subitem	Owner	Status	Goals	Notes
Define pilot boutiques + appointment types ...		Done		Last update: Drafted pilot (3 boutiques) + service types list. Next: Confirm with managers.
Confirm success metrics + targets (activation, ...		Done		Last update: Metrics drafted (activation, bookings/week, no-show rate). Next: Set Week 1–2 targets.
Draft workflow (before/after) + customer ...		In Progress		Last update: Mapped current booking flow. Next: Write "new flow" + client confirmation steps.

Task	Owner	Status	Due date	Notes	Priority
Testing 3		Not Started	Mar 19, 20...	Last update: UAT cases drafted. Next: Schedule pilot UAT; track issues to closure.	Medium

Subitem	Owner	Status	Goals	Notes
Write 8 UAT test cases (book, reschedule, cancel, confirmation)		Not started		Last update: Core flows outlined. Next: Add edge cases (double-booking, invalid time).
Run UAT session with 2 pilot users (30 min)		Not started		Next: Schedule 30-min pilot test; capture feedback + time-to-complete booking.
Log issues + retest fixes (severity: high/med/low)		Not started		Next: Tag severity; retest fixes and close out.

Task	Owner	Status	Due date	Notes	Priority
Launch + Support 4		In progress	Apr 2, 2027	Next: Publish go-live checklist + prepare Week 1 adoption update.	High

Subitem	Owner	Status	Goals	Notes
Go-live checklist (access, comms sent, support channel, escalation owner)		In Progress	· All pilot users have access + correct roles · Appointment types/ti...	· Last update: Checklist drafted; owners/contacts identified. · Next: Confirm access provisioning + send go-live message to pilot group.
Week 1 adoption snapshot + actions (activation, bookings, training)		Not started	· Activation rate: ≥70% of pilot users log in at least once · Training...	· Goal (Week 1): Activation ≥70%; Training ≥80%; 40+ bookings created. · Actual (sample): Activation 72%; Training 81%; 45 bookings. · Actions: Follow up with Boutique C; add...
Week 2 follow-up + improvements (refresher training, updated FAQ)		Not started	· Activation ≥80% · Training completion ≥90% · Bookings +20%...	· Goal (Week 2): Activation ≥80%; Training ≥90%; bookings +20% WoW. · Actual (sample): Activation 84%; Training 92%; 63 bookings. · Actions: Run 15-min refresher for Boutique C;...
Top issues log + mitigation		Not started	· Track top 3 issues + weekly actions	· Last update: Draft issue log categories (login, reschedule, notifications). · Next: summarize weekly + update FAQ/training.

Adoption Dashboard

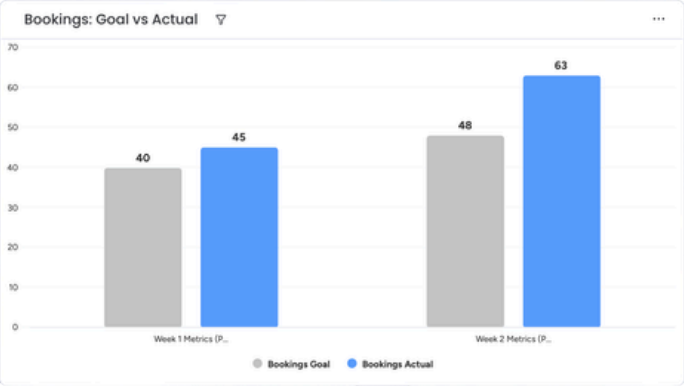

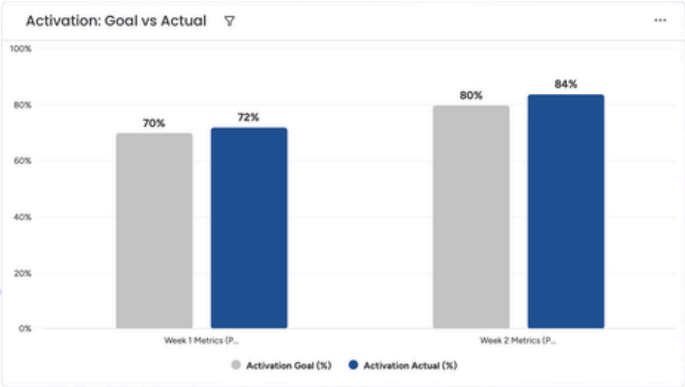

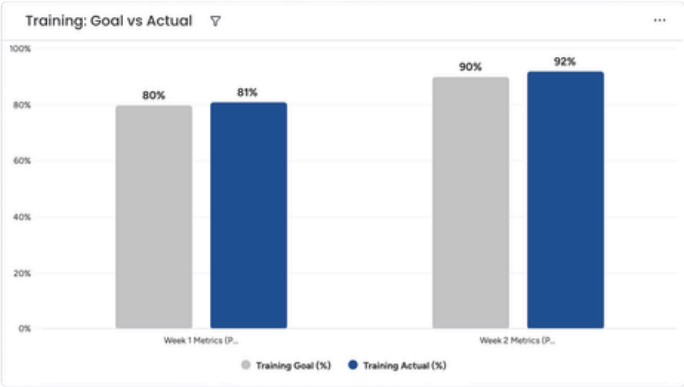

Adoption Reporting

Task	Activation Goal (%)	Activation Actual (%)	Training Goal (%)	Training Actual (%)	Bookings Goal	Bookings Actual
Week 1 Metrics (Pilot)	70%	72%	80%	81%	40	45
Week 2 Metrics (Pilot)	80%	84%	90%	92%	48	63

Week 1 Adoption Snapshot

Actions

- Follow up with boutiques with low activation
- Update rescheduling FAQ
- Send reminder message

Weekly Rollout Updates

Weekly updates tracked adoption metrics, user friction points, and follow-up actions during the pilot rollout.

Weekly Status Update – Week 1

Created at	Author	Status update	Replies	Thumbs
09/March/2027	Ruby Xia	**Week 1 adoption snapshot — results + actions** * **Goals (Wk1):** Activation ≥70% | Training ≥80% | 40+ bookings created * **Actuals (sample):** Activation 72% | Training 81% | 45 bookings created * **What's working:** Users are completing bookings end-to-end; confirmations are being sent successfully. * **Top friction points:** Rescheduling flow unclear for some associates; a few users needed support with login/access. * **Actions this week:** 1. * Follow up with Boutique C (low activation) and offer a 10-min walkthrough 2. * Add rescheduling FAQ + 1 screenshot to the quick guide 3. * Send a short reminder message with "3 steps to book + reschedule"	0	0
05/March/2027	Ruby Xia	**Go-live prep — checklist in progress** * **Status:** In progress * **This week:** Finalizing pilot access + appointment settings (time slots, service types, confirmation notifications). * **Completed:** Drafted go-live checklist and aligned on support/escalation path. * **Next:** Send go-live comms to pilot boutiques + attach quick guide + training deck. * **Risks/Watchouts:** Confirm notification settings to avoid missed confirmations; verify buffer times to prevent double-booking.	0	0

Week 2 follow-up + improvements

Created at	Author	Status update	Replies	Thumbs
12/March/2027	Ruby Xia	**Week 2 follow-up — improvements + next steps** * **Goals (Wk2):** Activation ≥80% | Training ≥90% | Bookings +20% WoW * **Actuals (sample):** Activation 84% | Training 92% | 63 bookings created * **What changed:** Adoption increased after refresher + updated quick guide. Rescheduling questions decreased. * **Open items:** Confirm whether all boutiques should use the same appointment types/time lengths or allow local flexibility. * **Next steps:** 1. * Finalize "standard appointment types" recommendation 2. * Maintain weekly adoption tracking (activation, training, bookings) 3. * Consolidate FAQs into a single page for broader rollout	0	0
